CENTRAL UNIVERSITY OF TECHNOLOGY

FACULTY OF ENGINEERING, BUILD ENVIRONMENT AND INFORMATION TECHNOLOGY

SUPACLEAN

LAUNDRY AND DRY-CLEANING MANAGEMENT SYSTEM

Year: 2026

PREPARED BY

GROUP H

NAME	STUDENT NUMBER
Masendeke CP	224043099
Mahlangu P	224014647
Maleke KT	222009259
Maema KE	224079714
Mojakwe KB	223032987
Moretlwe RK	221012635
Dasheka T	219007064

Leeu FD	223044569
Ntlati TT	224081629
Stallenberg BC	224081442

September 2026

TABLE OF CONTENTS

Project Introduction 5
Stakeholder and Organisation 5
Problem Statement 5
Project aim and Objectives 6
Project Scope 7
Project Deliverables 7
Acceptance Criteria 7
Inclusions 7
Constraints 7
Assumptions 8
Stakeholders and Users 8
Current Process 8
People involved 8
Information used 8
Current Process Diagram 9
Identified Problems 9
Product Perspective 10
Main product functions 10
Functional Requirements 10
Non-functional Requirements 11
Integration Requirements 11
Requirements Table 11
Technical feasibility 12
Operational feasibility 13
Economic feasibility 13
Schedule feasibility 13
Legal feasibility 13
Ethical feasibility 14
Feasibility conclusion 14

Project Risks 14
THREE HIGHEST RISKS 19
Requirements change log 19
Refined Scope 20
Refined Inclusions 20
Strict exclusions 20
Supporting evidence 20
25.1 Appendix A – Stakeholder Interview Questions and Responses 20
25.2 Appendix C – Evidence of Stakeholder Engagement 23
25.3 Appendix D – Stakeholder Confirmation of the Findings 24

Project Introduction

The SupaClean Laundry and Dry-Cleaning Management System is a proposed digital solution for SupaClean, a laundry and dry-cleaning business that operates through multiple pickup and drop-off points. Customers currently take their clothing to these locations, where the items are received and each clipped with a waterproof paper of a certain colour depending on the location from which the laundry was collected from. The clothing is then collected by employees or drivers and transported to the main SupaClean facility for washing, dry cleaning, and pressing where necessary. Once the process is complete, the clothing is returned to the relevant pickup point for collection by the customer.

The project aims to develop a digital platform consisting of a Flutter mobile application for customers and an ASP.NET web application for employees and management, supported by a Supabase database. The system is intended to improve communication between SupaClean and its customers while providing authorised employees with a centralised way to manage customer and order information.

The main stakeholder for the project is Tim, the manager of SupaClean, who identified the need for a digital system that can improve customer interaction and assist the business in managing relevant order information.

Stakeholder and Organisation

Organisation: SupaClean

Type: Laundry and dry-cleaning business

Stakeholder: Tim

Role: Manager

Contact: 051 430 4241or 0664702253

SupaClean is a laundry and dry-cleaning business that uses different pickup/drop-off points. Customers leave their clothes at these locations, and employees collect the clothes and take them to the main facility for washing or dry cleaning. Once completed, the clothes are returned to the pickup point for the customer to collect them.We selected SupaClean because the stakeholder identified areas where the business could benefit from a digital system, particularly in communicating with customers and managing order information.

Problem Statement

SupaClean currently uses physical pickup points and a ticket or docket system to manage customer laundry and dry-cleaning orders. Although the existing process supports the movement and processing of customer items, customer and order information is not connected through a single integrated digital platform.

As a result, customers have limited digital access to information about their orders and may need to rely on manual communication or physical interaction with pickup points. Employees also need to manage customer and order information throughout the different stages of the laundry and dry-cleaning process without a centralised digital platform.

The problem affects several users:

Customers have limited access to digital order information and communication.

Employees need to manage and communicate order information across different stages of the process.

Management requires a better way to oversee relevant customer and order information.

The consequences of the current situation include increased reliance on manual communication, limited customer access to order information, difficulties communicating exceptional issues relating to customer items, reduced digital interaction with the business, and potential challenges in attracting and retaining customers.

Therefore, an improved digital solution is needed to provide customers and authorised employees with easier access to relevant information and improve communication surrounding the existing laundry and dry-cleaning process.

Project aim and Objectives

Project Aim

The aim of the project is to develop a mobile and web-based Laundry and Dry-Cleaning Management System that improves the way SupaClean manages customer and order information while providing customers with a more convenient way to interact with the business.

Project Objectives

The project aims to achieve the following objectives:

Allow customers to view the laundry and dry-cleaning services offered by SupaClean.

Allow customers to submit laundry or dry-cleaning requests through the mobile application.

Allow customers to view relevant information about their orders.

Allow authorised employees to view and manage customer orders through the system/dashboard.

Allow employees to update the status of an order as it progresses through the process.

Allow customers to receive important notifications relating to their orders.

Provide a way for SupaClean to communicate relevant information when exceptional situations occur.

Allow SupaClean to display specials and promotional information to customers.

Provide management with access to relevant customer and order information.

Project Scope

Project Deliverables

The project will deliver the following:

A Flutter mobile application mobile application version for SupaClean customers and authorised employees/management

An ASP.NET web application web application version for SupaClean customers and authorised employees and management.

A Supabase database for storing and managing relevant system data.

A Supabase authentication for authenticating users and employees

Project documentation describing the analysis, design, development, and testing of the proposed system.

Acceptance Criteria

The primary acceptance criterion for the system is that:

A customer must be able to submit an order through the proposed system, and an authorized employee must be able to view and manage that order through the web application.

Additional functionality should support the objectives of allowing customers to access relevant order information and allowing employees to update and manage order statuses.

Inclusions

The following features are outside the scope of the project:

Home pickup and delivery services.

Live driver tracking.

Online payment gateway integration.

Key-cutting services, carpet washing and cleaning products sale.

Replacement of SupaClean's existing ticket or docket system.

Live tracking of the stages which the laundry undergoes.

The proposed system is intended to support and improve the existing business process rather than completely replace all existing operational systems.

Constraints

The project is subject to the following constraints:

Limited time available during the semester or project period.

Limited development experience within the project team.

The system must be designed, developed, and completed within the required academic project period.

Assumptions

The project is based on the following assumptions:

The stakeholder will be available to provide feedback when required.

SupaClean's existing ticket or docket system will continue to be used.

Customers will continue to make payments face-to-face during the prototype stage.

Project requirements may be refined or changed based on stakeholder feedback.

Authorized employees will have access to the web application to manage relevant orders.

Stakeholders and Users

Stakeholder or User	Role in the proposed system
External stakeholder	Manager
Mobile Application user	Employees, Clients and Stuff
Web application user	Employees, Clients and Stuff
Other affected users	N/A

Current Process

A customer takes their clothes to one of the SupaClean pickup points. The employee receives the clothes and uses the company's existing ticket/docket system. An employee/driver then collects the clothes and takes them to the main facility. The clothes are washed or dry cleaned and pressed where necessary. Once completed, they are taken back to the pickup point where the customer collects them.

People involved

- Customers
- Pickup-point employees
- Drivers/collection employees
- Cleaning employees
- Management

Information used

- Customer details

- Ticket/docket number
- Items received
- Service requested
- Price
- Pickup point
- Order status
- Collection information

Customer
↓
Pickup / Drop-off Point
↓
Employee / Driver
↓
Main SupaClean Facility
↓
Washing / Dry Cleaning
↓
Employee / Driver
↓
Pickup / Drop-off Point
↓
Customer

Current Process Diagram

Identified Problems

The stakeholder identified that SupaClean could benefit from a digital system that improves communication with customers and provides better management of customer and order information.

Currently, customers mainly interact with SupaClean through physical pickup points and existing communication methods. There is no integrated digital platform that connects customers and authorized employees to information about the progress of an order.

Exceptional situations may also occur during the cleaning process. For example, an employee may discover a difficult stain or determine that a particular chemical could potentially damage an item. In these situations, SupaClean may need to communicate with the specific customer before continuing with the cleaning process.

Product Perspective

The system will consist of a Flutter mobile application for customers and employees an ASP.NET web application for employees and management. Customers will be able to view services, place requests, select a pickup point and receive order updates. Employees will use the web application to view orders and update their progress. Both applications will connect to the same Supabase database, allowing information to be shared and kept up to date across the system.

Main product functions

Component	Main Functions
Flutter mobile application	Customers can view services, place laundry/dry cleaning requests, select a pickup point and receive order updates and notifications
ASP.NET web application	Management can view customer orders, manage orders, update order statuses and manage service information
Supabase backend	Stores and manages customer, order, service and pickup point information, and connect the mobile app with the web application

Functional Requirements

FR1: The customer must be able to browse laundry services, register and log in to their account, track their laundry status, request delivery, receive notifications, and view their orders through the Flutter application.

FR2: The administrator must be able to log in, view and accept or reject orders, update laundry statuses, manage customers, and manage deliveries through the system.

FR3: The driver must be able to view assigned orders, confirm deliveries and collections, and update the collection status through the application.

Non-functional Requirements

NFR1: The system must support the versions agreed upon during the requirements analysis.

NFR2: The system must maintain data integrity by preventing orders from being matched with the wrong customer.

NFR3: The system must use a modular architecture to allow components to be easily decoupled and maintained.

NFR4: The system must require users to authenticate before accessing protected functionality.

NFR5: The system should be available during and after the stakeholder's operating hours.

Integration Requirements

IR1: The application and web system must integrate with Supabase PostgreSQL to securely store and manage application data.

IR2: The application and web system must integrate with Google Maps to provide accurate locations of the various depots.

IR3: The application and web system must integrate with Supabase Authentication to provide secure user registration, login, and authentication services.

Requirements Table

ID	Requirement	Type	Priority	Related stakeholder need
FR1	Customers must browse services, register, log in, track laundry, request delivery, receive notifications, and view orders.	Functional	Must Have	Improve customer service
FR2	Administrators must log in, manage orders, customers, laundry statuses, and deliveries.	Functional	Must Have	Improve business management
FR3	Drivers must view assigned orders, confirm	Functional	Must Have	Improve delivery and collection

	collections/deliveries, and update statuses.			management
NFR1	The system must support agreed software versions.	Non-functional	Should Have	Ensure system compatibility
NFR2	The system must prevent orders from being linked to the wrong customer.	Non-functional	Must Have	Protect customer data
NFR3	The system must use a modular architecture.	Non-functional	Should Have	Improve maintainability
NFR4	Users must authenticate before accessing protected features.	Non-functional	Must Have	Ensure security
NFR5	The system should be available beyond operating hours.	Non-functional	Should Have	Ensure availability
IR1	The system must integrate with Supabase PostgreSQL.	Integration	Must have	Store application data
IR2	The system must integrate with Google Maps.	Integration	Should have	Locate depots
IR3	The system must integrate with Supabase Authentication.	Integration	Must Have	Secure user access

Technical feasibility

Selected: Feasible with changes

The proposed technologies Flutter, ASP.NET, and Supabase are suitable for developing the system and do not require specialised hardware. However, the team has limited experience with some of these

technologies and using both mobile and web frameworks may increase the learning curve. The system also does not directly integrate with the existing paper-based ticket system, which may require duplicate data entry during the prototype phase. Therefore, some features may need to be simplified or prioritised to fit the available development time and team skills.

Operational feasibility

Selected: Feasible with changes

The proposed system is suitable for customers, employees, and management because it improves order tracking, customer communication, and delivery management. However, employees may have to use both the existing paper-based system and the new digital system, which could increase their workload. Some users may also require training to use the system effectively. Therefore, the system is operationally feasible but may require a simpler employee workflow, training, and future integration with the existing system.

Economic feasibility

Selected: Feasible

The system can be developed using mostly free technologies such as Flutter, ASP.NET, and Supabase, with minimal hardware and hosting costs during the prototype phase. The main cost is the development time of the team. Therefore, the project is economically feasible within the available resources, although additional costs may be required for hosting, hardware, and training if the system is continued after the prototype stage.

Schedule feasibility

Selected: Feasible with changes

The project can be completed within the available semester if the team focuses on the minimum viable product (MVP). Developing both the Flutter mobile application and ASP.NET web application within a limited time may be challenging, especially with limited development experience. Core features such as order submission, order management, and order status tracking should be prioritised, while notifications and promotions can be postponed if necessary. Regular testing, stakeholder feedback, and bug fixing should also be included in the schedule.

Legal feasibility

Selected: Feasible with changes

The project is legally feasible because it can comply with South African data protection requirements under POPIA. However, the system will handle customer and order information, so proper

authentication, access control, secure data storage, and data minimisation must be implemented. A basic privacy notice should also be provided, and sensitive information such as passwords and API keys must not be stored in public repositories.

Ethical feasibility

Selected: Feasible with changes

The project is ethically feasible if customer and employee information is handled responsibly and fairly. Customers should be informed about how their information is used, while employees should only access information relevant to their roles. The app should remain optional during the prototype phase so that customers without smartphones or with limited digital skills are not excluded. Clear communication, accurate order information, and honest promotions should also be maintained.

Feasibility conclusion

The proposed project is feasible with changes.

The main strengths of the project are the availability of suitable development technologies, low development costs, and the ability to address the stakeholder's need for improved laundry order and customer management.

The main limitations identified are the limited development experience of the group, the development of both a Flutter mobile application and an ASP.NET web application, the fixed semester deadline, and the need to comply with privacy and security requirements.

To ensure that the project can be completed within the semester, the group will prioritise the essential MVP functions, control the project scope, simplify or postpone lower-priority features, and allocate sufficient time for testing and stakeholder feedback.

Project Risks

LIKELIHOOD 1 = Unlikely • 2 = Possible • 3 = Likely	IMPACT 1 = Low • 2 = Medium • 3 = High	RISK LEVEL 1–3 Low • 4–6 Medium • 7–9 High

ID	RISK STATEMENT	CATEGORY	LIKELIHOOD (1-3)	IMPACT (1-3)	SCORE	LEVEL	MITIGATION ACTION	CONTINGENCY ACTION	RISK OWNER	STATUS
R01	Limited group experienc	Technical	3	3	9	High	Test basic Supabase functions	Simplify database functions	Backend Develo	Monitoring

	e with Supabase may delay development of the database and connections between application components.						early and allocate learning tasks to group members.	and use tested core features if integration problems occur.	per	
R02	Difficulty linking the existing ticket/docket system with the proposed digital order may delay order-management functionality.	Technical / Integration	3	3	9	High	Investigate the existing ticket system early and test how ticket numbers can be associated with digital orders.	Use authorised employee manual entry of the existing ticket number as the MVP approach.	Technical Lead	Monitoring
R03	Flutter and ASP.NET development tasks may take longer than planned,	Schedule / Technical	3	3	9	High	Break development into smaller tasks and test each component as it is complete	Prioritise essential MVP functions and postpone non-essential features.	Project Manager	Open

	leaving insufficient time for testing and final improvements.						d.			
R04	The stakeholder may become unavailable or delay feedback, which could delay confirmation of requirements and system decisions.	Stakeholder	2	3	6	Medium	Arrange important stakeholder meetings and feedback dates in advance.	Use previously confirmed requirements and request written feedback where possible.	Stakeholder Liaison	Monitoring
R05	Too many proposed functions may prevent the group from completing the prototype within the semester.	Scope	2	3	6	Medium	Prioritise the agreed MVP functions before developing secondary features.	Remove or postpone promotions, referrals and other lower-priority functions.	Project Manager	Monitoring
R06	A group member may not complete	Team	2	3	6	Medium	Assign clear responsibilities and	Reassign urgent tasks to available	Project Manager	Open

	an assigned task on time, which could delay activities that depend on that work.						review task progress during weekly group meetings.	members and record the contribution concern.		
R07	Unclear or changing pricing and service requirements may result in incorrect price-estimation functionality.	Requirements / Quality	2	2	4	Medium	Obtain the stakeholder's confirmed price list and service rules before finalising pricing.	Use estimated pricing or temporarily disable the affected calculation until requirements are confirmed.	Business Analyst	Monitoring
R08	Limited access to reliable internet, suitable development devices or required software may interrupt developm	Resources	2	2	4	Medium	Confirm access to required development tools and arrange alternative working arrangements where necessary	Share project resources or allow affected members to use another available device.	Project Manager	Open

	ent activities.						.			
R09	Incorrect handling of customer information or system credentials may expose personal information or allow unauthorised access.	Data / Security	2	3	6	Medium	Use secure authentication, appropriate permissions and avoid sharing Supabase credentials.	Change compromised credentials, restrict access and investigate the affected account or data.	Backend / Security Lead	Monitoring
R10	Limited testing across the Flutter application, ASP.NET components and Supabase backend may allow defects to remain in the prototype.	Quality / Technical	3	3	9	High	Create test cases for customer, employee and administrator workflows and test throughout development.	Fix critical defects first and postpone non-essential functions until testing is complete.	QA / Testing Lead	Open
R11	Incorrect or delayed order-	Operational / Quality	2	3	6	Medium	Define clear order statuses	Allow an administrator to correct	Employee Interface Lead	Open

	status updates may cause customers to receive inaccurate information about their laundry or dry-cleaning orders.						and test employee update workflows.	the status and contact the customer if necessary.		

9 – High	**1. R01 – Limited Supabase experience** **Supabase is the central database/backend. Test basic database and integration functions early.**

THREE HIGHEST RISKS

9 – High	**2. R02 – Existing ticket/docket integration** **The proposed system must work alongside SupaClean's existing ticket process. Investigate the system and test manual ticket-number linking.**

9 – High	**3. R03 – Flutter/ASP.NET development delays** **Delays could reduce testing time. Prioritise the core MVP and monitor progress against the schedule.**

Requirements change log

Original Requirement	Change Made	Reason for Change
Marketing not considered	Sharing of app equals discount	To enhance marketing and access of application along with

		business
App created for one store	App must integrate with various depots	The Dry Clean has many branches with one central factory
Only Dry Cleaning Services Considered	Other services provided by dry clean included e.g carpet cleaning	To create a centralised app for all services provided by the dry clean business
All customer delivery fee are the same	Customer not within a certain radius to the nearest depot will be provided discount while customer in a certain radius wont	This is to keep the depots operational and promote dropping off at depots where possible

Refined Scope

Refined Inclusions

The service catalogue will included not only standard dry cleaning services but also specialized services like carpet washing

Multi-depot support to allow customers to select drop off/pickup points catering to SupaClean's multi-depot model

App will include basic marketing features e.g app sharing discounts

System will not replace the existing manual ticket/docket system

Strict exclusions

Live Driver Tracking

Direct online payment integration

Automated Replacement of existing ticket/docket system

Supporting evidence

25.1 Appendix A – Stakeholder Interview Questions and Responses

Business Background Question: Can you tell us about SupaClean and the services you provide? Answer: SupaClean is a laundry and dry-cleaning business. Question: How does the current SupaClean process work from the customer's point of view? Answer: Customers leave their clothes at different

pickup/drop-off points. Employees collect the clothes and take them to the main SupaClean facility, where the clothes are washed or dry cleaned and pressed where necessary. Once completed, the clothes are returned to the pickup point for the customer to collect. Question: What locations or points are involved in the process? Answer: SupaClean uses different pickup/drop-off points where customers leave and collect their clothes.

Current Process and Information Question: How are customer orders currently recorded? Answer: The business currently uses an existing ticket/docket system. Question: What information is used when processing an order? Answer: The information includes customer details, ticket/docket number, items received, service requested, price, pickup point, order status, and collection information. Question: Who is involved in processing customer orders? Answer: Customers, pickup-point employees, drivers or collection employees, cleaning employees, and management are involved. Question: What happens after clothes are received at a pickup point? Answer: An employee or driver collects the clothes and takes them to the main facility for washing or dry cleaning. Question: What happens once the cleaning process is completed? Answer: The completed clothes are taken back to the pickup point, where the customer collects them.

Current Problems and Challenges Question: What are the main challenges you would like to improve in the business? Answer: SupaClean would like to bring back existing customers and attract new customers. The business would also like to improve how customers interact with SupaClean and how customer and order information is managed. Question: How do customers currently interact with SupaClean?


Answer: Customers mainly interact with the business through the physical pickup points and existing communication methods. Question: What would you like to improve about customer interaction? Answer: SupaClean would like a digital system that makes it easier for customers to interact with the business. Question: Are there situations where employees need to communicate with a specific customer about an order? Answer: Yes. There can be exceptional situations, such as a difficult stain or an item that may be damaged by certain chemicals. In these situations, the business may need to communicate with the specific customer. Question: What difficulty does this create? Answer: The business needs a way to communicate with the specific customer when there is an issue with an item or order. 4. Customers Question: What would customers need from a digital system? Answer: Customers should be able to view services, place laundry or dry-cleaning requests, select a pickup point, view order information, and receive important notifications. Question: What information should customers be able to access? Answer: Customers should be able to access relevant information about their services and orders. Question: Why would improving digital customer interaction be useful to SupaClean? Answer: It could make it easier for customers to interact with SupaClean and support the business's goal of bringing back existing customers and attracting new customers. 5. Employees and Management Question: What would employees need to do using the system? Answer: Authorised employees would need to manage customer and order information and update order statuses during the different stages of the process. Question: What would management need from the system? Answer: Management would need to oversee orders and customer information. Question: Who should have access to customer and order information? Answer: Access should be provided to authorised employees and


management according to their responsibilities. 6. Digital Solution Requirements Question: What would you want a digital system to help SupaClean achieve?


Answer: The system should make it easier for customers to interact with SupaClean and help the business manage relevant customer and order information. Question: Should the new system replace the existing ticket/docket system? Answer: No. The existing ticket/docket system will continue to be used for the prototype. Question: What features are currently being considered for the system? Answer: The initial scope includes allowing customers to view services, place laundry or dry-cleaning requests, select a pickup point, view order information, receive important notifications, and view SupaClean specials and promotions. Employees should be able to manage orders and update statuses. Question: What should happen when there is an exceptional problem with an item? Answer: The system should support communication with the specific customer when there is an issue such as a difficult stain or a possibility that an item could be damaged by certain chemicals. 7. Project Scope Question: What should the initial project focus on? Answer: The initial project should focus on improving digital customer interaction and managing relevant customer and order information. Question: What features are currently outside the project scope? Answer: Home pickup and delivery, live driver tracking, online payment gateways, payroll, shoe cleaning and key cutting management, and replacing the existing ticket/docket system are outside the initial scope. Question: What would be an acceptable result for the prototype? Answer: A customer should be able to submit an order and an authorised employee should be able to view and manage that order through the web application. 8. Stakeholder Expectations Question: What do you expect from the proposed system? Answer: The system should make it easier for customers to interact with SupaClean and help authorised employees manage customer and order information. Question: How should the project team work with SupaClean during development? Answer: The stakeholder should provide feedback when required, and requirements can be reviewed and adjusted after stakeholder feedback. Question: Are there any limitations the project team should consider? Answer: The project has limited time and development experience. Access to SupaClean's existing system may not be available. The existing ticket/docket system will continue to be used, and requirements may change after further stakeholder feedback. 9. Closing Questions

Question: If you could improve one part of the current customer experience, what would you improve? Answer: The priority is to make it easier for customers to interact with SupaClean through a digital system. Question: What would make the proposed system useful to SupaClean? Answer: It should improve customer interaction and make relevant customer and order information easier for the business to manage. Question: Are there any additional requirements or concerns we should consider before development? Answer: Requirements may change after further stakeholder feedback, so continued engagement with SupaClean will be necessary.

25.2 Appendix C – Evidence of Stakeholder Engagement

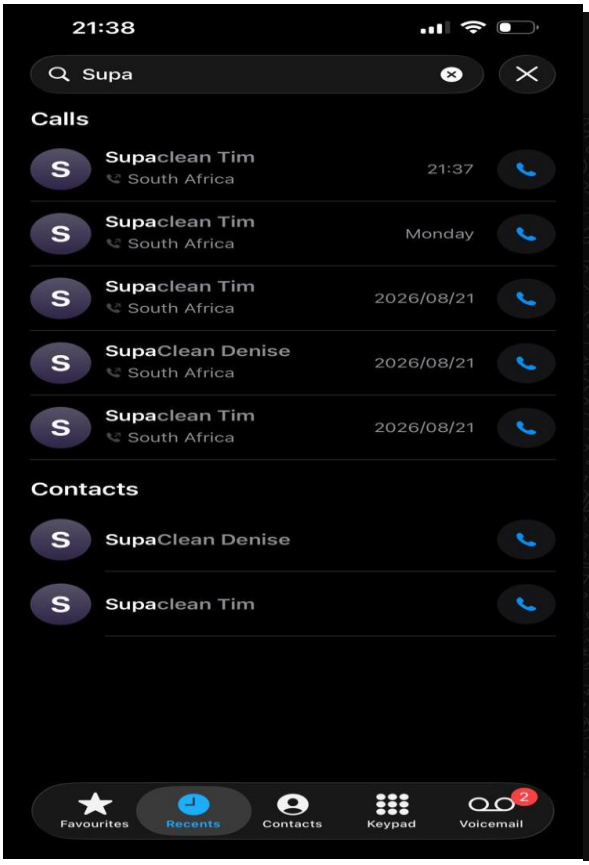

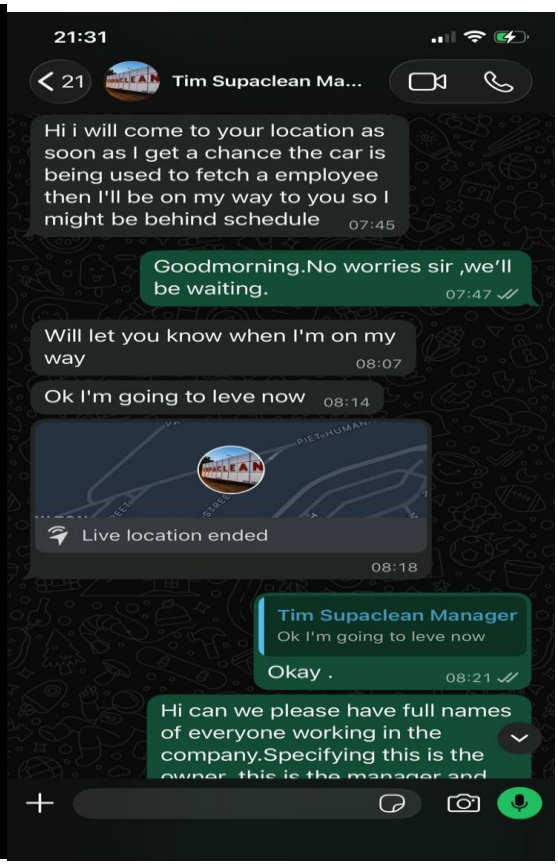

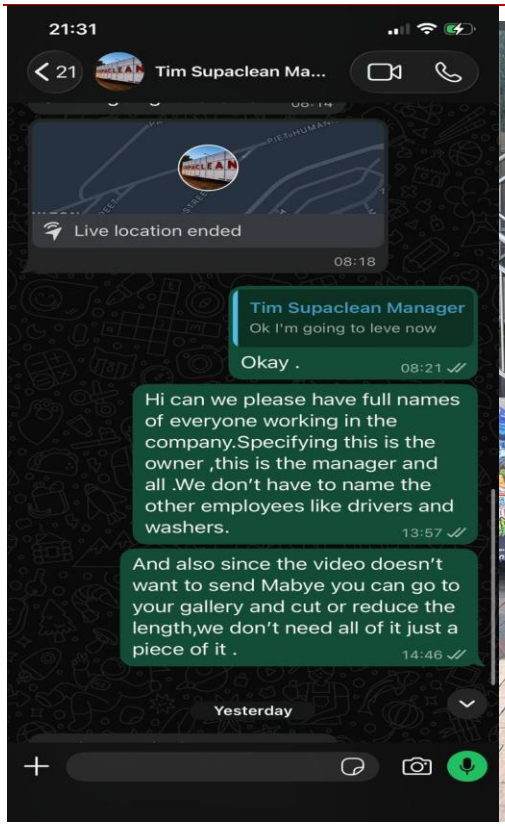



25.3 Appendix D – Stakeholder Confirmation of the Findings

Stakeholder Overview Name: Tim Role/Title: Manager Organization: SupaClean Phone: 051 430 4241 or 0664702253 Location: Bloemfontein, South Africa

Stakeholder Interests Primary Goals: To bring back existing customers, attract new customers, and improve how customers interact with SupaClean. Key Interests: Improving customer communication, managing customer and order information, allowing customers to access services and order information digitally, and communicating with customers when exceptional problems occur with an item. Motivations: To improve customer interaction with the business and make relevant customer and order information easier to manage.

Stakeholder Influence Level of Influence: High Decision-Making Power: The stakeholder can provide business requirements, approve or reject proposed features, and provide feedback on whether the system meets the needs of SupaClean. Key Relationships: Customers, pickup-point employees, drivers/collection employees, cleaning employees, and management.

Stakeholder Expectations Expectations from the Project: A digital solution that makes it easier for customers to interact with SupaClean and helps authorised employees manage customer and order information. Preferred Communication Style: Meetings and direct discussions with the project team. Feedback Frequency: At important project stages and whenever stakeholder feedback is needed to confirm requirements or review the prototype.

Challenges and Concerns Potential Challenges: Access to SupaClean's existing ticket/docket system may not be available; requirements may change after further discussions; the business's current processes must be understood properly before developing the solution.

Concerns: The new system should support the existing business process rather than unnecessarily replacing it. Customer and order information should be accessible only to authorised users. The system should also make it possible to communicate with customers about exceptional issues, such as difficult stains or items that could be affected by certain chemicals. Conflict Resolution Approach: Discuss disagreements directly with the stakeholder, clarify the business requirement, document the agreed decision, and prioritise the stakeholder's confirmed needs within the project scope.

6. Engagement Plan Engagement Strategies: Conduct interviews and meetings, confirm requirements, demonstrate wireframes/prototypes, collect feedback, and review the system at important development stages. Key Milestones for Engagement:

Requirements confirmation

Review of proposed system features

Review of initial design/prototype

Testing and feedback

Final evaluation Communication Plan: Communicate through scheduled meetings and direct contact when important decisions or feedback are required.

1. Notes and Additional Information

SupaClean uses different pickup/drop-off points.

Customers leave clothes at a pickup point.

Employees/drivers transport the clothes to the main facility.

Clothes are washed or dry cleaned and pressed where necessary.

Completed clothes are returned to the pickup point for collection.

The existing ticket/docket system will continue to be used for the prototype.

The initial project focuses on improving digital customer interaction and managing relevant customer and order information.

Home pickup and delivery, live driver tracking, online payments, payroll, shoe cleaning, key cutting, and replacing the existing ticket/docket system are currently outside the initial scope.
